

ENTERPRISE PORTFOLIO


STEM RACING 2025/2026 - NATIONAL FINALS

PROJECT MANAGEMENT - BRAND - MARKETING - SPONSORSHIP - SUSTAINABILITY

PORTFOLIO BRIEF

A dense enterprise portfolio built with the same high-information structure as the reference portfolios while keeping the RevolutionX black and gold identity, sponsors, team story and complete original index.

SPONSORS AND INSTITUTIONAL SUPPORT



WELCOME TO OUR JOURNEY	
TABLE OF CONTENTS	
1. Project Management	25. Name
2. Kick Off Meeting	26. Colour Scheme
3. Project Charter	27. Logo
4. Scope Statement	28. Uniform
5. Work Breakdown Structure (WBS)	29. Marketing
6. Schedule	30. Marketing Goals
7. Budget & Resource Management	31. Target Audiences
8. Resource Management	32. Taking Action
9. Budget Spend Tracking (Base vs Original)	33. Instagram
10. Roles & Responsibilities	34. Website
11. Team Structure	35. Nova Alliance
12. Team Members	36. High School Open House
13. Role Descriptions	37. Newspaper Articles
14. RACI Chart	38. Visit by the Mayor of Majadahonda
15. Team & Stakeholder Communications	39. Sponsorship
16. Stakeholder Register	40. Overview
17. Communication Tools	41. Sponsorship Strategy
18. Communication Plans	42. Sponsorship Recruitment
19. Risk Management	43. Return on Investment (ROI)
20. Risk Identification, Planning, Analysis & Assessment	44. Crowdfunding
21. Monitoring & Controlling	45. Sustainability
22. Status Reports	46. Biodegradable PLA
23. Sponsorship & Marketing	47. Battery Collection Campaign
24. Team Identity	

KICK-OFF MEETING

On 30 April, the day after the Madrid regional competition, RevolutionX held its first meeting ahead of the national finals of the 2025/2026 season. The team had achieved its first goal, a place at the national finals on 16 June, yet the regional performance left a bittersweet feeling. The team understood that qualifying for the international finals would require improvement across the board and a real reinvention.

The meeting established that the national finals would be approached differently. The natural starting point for the project was to answer the WH questions: who, why, what, when, where and how. These answers became the base for the project charter and project management direction.

TEAM	SCHOOL
RevolutionX	IES Jose Saramago
CATEGORY	FINALS DATE
Professional	16 June

PROJECT DEFINITION	
SIX WH QUESTIONS	
QUESTION	ANSWER
Who are we?	RevolutionX, a STEM Racing team made of Year 10 and 11 students from IES Jose Saramago in Majadahonda.
Why compete?	After the first year in the competition, the team is genuinely passionate about STEM Racing and wants to qualify for the international finals.
What must be done?	Submit two portfolios, prepare a verbal presentation and design and build a car for a 20-metre track.
When start?	The day after the regional competition, because more working time creates a competitive advantage.
Where measure success?	First at the Madrid regional finals, then by reaching the podium in the Professional category at nationals.
How do we see ourselves?	As a reinvented team with an improved car and one of the strongest brand identities in the competition.
PROJECT CHARTER PURPOSE	

The project charter is the formal document that marks the official start of the project. It defines the purpose, objectives, key milestones, responsible people, constraints and anticipated risks. Its primary function is to act as an initial agreement: what will be done, why it matters and who will carry it out.

For RevolutionX, this shared written understanding prevents misunderstandings and deviations across engineering, enterprise, sponsorship, marketing and communication work.

OFFICIAL START	
REVOLUTIONX PROJECT CHARTER	
FIELD	CONTENT
Project	STEM Racing 2025/2026
Team name	RevolutionX
Date	04/04/2026
Project managers	Saul Moran and Martin Cendra
Team members	Martina Corredor, Victor Jimenez, Yago Alvarez and Alvaro Cardona
Project description	A competition for students aged 12 to 19 based on the design and construction of a miniature racing car and the development of an original brand.
Project justification	A personal and professional growth opportunity and a competitive challenge to improve the results achieved at the regional competition.

MILESTONES, ACCEPTANCE AND RISKS

MILESTONE	ESTIMATED DATE
Project initiation	June 2025
Deliverables commencement	September 2025
First submission of deliverables	April 2026
Regional competition	April 2026
Second submission of deliverables	June 2026
National competition	June 2026

- >> Acceptance criteria: a task is complete only once the relevant department coordinator gives formal sign-off.
- >> Assumption: the Professional category at nationals will be highly competitive, leaving no room for complacency.
- >> Constraint: only around one hour of school working time per day is available.
- >> Main risks: task deadline failure and car damage or mechanical failure shortly before the competition.

SCOPE STATEMENT

The scope statement determines how far the project can go and what is within the team's control. RevolutionX defined the project objective as qualification for the international finals and separated what the team could directly manage from constraints outside its control.

SCOPE FIELD	REVOLUTIONX DEFINITION
Project managers	Martin Cendra and Saul Moran
Date	September 2025 - June 2026
Name	RevolutionX STEM Racing National Finals Project
Objective	Qualification for the international finals
In scope	Submission of deliverables and acquisition of resources
Out of scope	Working time at school and fundamental resources such as machinery
Acceptance	Coordinator approval for the relevant sector
Deliverables	Car, sponsorship prospectus, enterprise portfolio, engineering portfolio, resource search, uniform and social media
Constraints	Budget: 1100 EUR; team size: 6 members plus 2 assistants; 2 months since regional finals; limited school time

SCOPE BASELINE

WORK BREAKDOWN STRUCTURE (WBS)

The WBS visualises the phases and stages of the most important deliverables. It breaks large outcomes into manageable work packages so each area can be planned, assigned and monitored.

AREA	DELIVERABLE	STAGES
Engineering	Car	Conceptualisation - sketch - 3D modelling - testing - refinement - manufacturing
Engineering	Wind tunnel	Conceptualisation - structure design - 3D modelling - part printing - assembly
Engineering	Technical portfolio	Conceptualisation - sketch - refinement - graphics - final refinement
Business	Sponsorship prospectus	Conceptualisation - sketch - refinement
Business	Nova Alliance	Collaboration with Owla - strategy - contact - publication
Business	Uniforms	Conceptualisation - prototyping - refinement - manufacturing
Business	Pit display	Brainstorming - prototyping - reference analysis - refinement

SCHEDULE MANAGEMENT

The organisational schedule is one of the key tools for RevolutionX. It is based on a Gantt chart and is updated roughly every month to keep the project organised. The chart shows start dates, end dates and task durations, allowing the team to understand when work will finish and how to plan around deadlines.

SCHEDULE BASELINE - GANTT VIEW											
	JUN	JUL	AUG	SEP	OCT	NOV	APR	MAY	JUN	FINAL	
Project initiation											
Deliverables commencement											
Technical and enterprise portfolios											
Sponsorship prospectus											
Uniforms and pit display											
Regional competition											
Second deliverable submission											
National competition											

COST CONTROL

BUDGET & RESOURCE MANAGEMENT

Effective resource management is essential for allocating available funds and materials. RevolutionX identified two critical investment areas: the Pit Display and CNC manufacturing of the car.

At the start of the national-finals campaign, the enterprise coordinator estimated that the team would need around 1000 EUR to buy the desired competition elements. After sponsors and crowdfunding brought the team close to the target, RevolutionX carried out a detailed search for everything it wanted to purchase.

The estimate proved accurate: the total price of all the items bought for the competition was 1033 EUR.

ESTIMATED NEED 1000 EUR	ACTUAL SPEND 1033 EUR
MAIN INVESTMENTS Pit + CNC	CONTROL METHOD Spend tracking

RESOURCE CATEGORY	MANAGEMENT DECISION
Pit Display	Prioritised because it represents the team and brand at the competition.
CNC manufacturing	Prioritised because car production is a technical critical path item.
Sponsors	Used to secure monetary and material resources.
Crowdfunding	Used when sponsorship alone was not enough to cover all expenses.

TEAM STRUCTURE

A key factor in RevolutionX's success has been the designation of two project coordinators: one focused on engineering and another focused on business management. This structure provides better oversight and coordination while preserving cross-functional collaboration.

The team is made of versatile students, which allows members to support different departments. RevolutionX also benefited from student volunteers who could not officially compete because all positions were already filled, yet still contributed to the project.

CORE TEAM 6	ASSISTANTS 2
COORDINATORS 2	STRUCTURE Dual sector

TEAM MEMBERS

MEMBER	ROLE	SKILLS	KNOWLEDGE
Saul Moran	Team Coordinator	Excel, Canva, GIMP, ClickUp	Finance, organisation, graphic design
Martin Cendra	Team Manager	Fusion 360, Antigravity, Visual Studio Code	AI usage, programming, engineering
Martina Corredor	Strategy, Engineering & External Relations	Canva, SimScale, Prezi	Graphic design, communication, engineering
Victor Jimenez	Design Engineer	Fusion 360, DaVinci Resolve	Engineering, aerodynamics, 3D printing
Yago Alvarez	Communication & Social Media	BeFunky, Instagram, Prezi, Canva, CapCut	Communication, graphic design, video editing
Alvaro Cardona	Manufacturing Engineer	Fusion 360, Ansys, Blender	Aerodynamics, simulation, 3D printing, engineering
Claudia de Paz	Business Management Assistant	Canva, BeFunky	Communication, graphic design
Ibrahim Aharrar	Engineering Assistant	Fusion 360	Engineering, aerodynamics

ACCOUNTABILITY

ROLE DESCRIPTIONS

Although RevolutionX is a highly collaborative team, clearly defined roles are essential for specialisation, personal development and collective performance. Roles were assigned according to software proficiency and knowledge in each sector.

TEAM COORDINATOR - SAUL MORAN Saul organises business management tasks, breaks large projects into smaller tasks and assigns them across the team. His organisational skills help divide objectives effectively. He also manages the team's finances and accounts.
TEAM MANAGER - MARTIN CENDRA Martin oversees engineering, organises design and testing plans and designed the website using tools such as Antigravity. His role differs from Saul's because it focuses on engineering strategy and technical delivery.
STRATEGY, ENGINEERING & EXTERNAL RELATIONS - MARTINA CORREDOR Martina connects engineering and enterprise. She assists engineers with simulation testing and contacts external companies and media outlets such as RTVE, EL MUNDO and El Espanol.
DESIGN ENGINEER - VICTOR JIMENEZ Victor brings the car to life. After designing Spain's fastest Entry car the previous year, he works on a completely new Professional-class car and aims for the same level of competitive performance.

ROLE DESCRIPTIONS CONTINUED

COMMUNICATION & SOCIAL MEDIA - YAGO ALVAREZ Yago is responsible for communication on competition day and for the team's Instagram content. He designs most posts and supports the public-facing side of the brand.
MANUFACTURING ENGINEER - ALVARO CARDONA Alvaro performs simulation work and leads one of the most important projects: the wind tunnel, enabling more realistic aerodynamic testing.
BUSINESS MANAGEMENT ASSISTANT - CLAUDIA DE PAZ Claudia supports business management with communication and graphic design tasks.
ENGINEERING ASSISTANT - IBRAHIM AHARRAR Ibrahim supports engineering and aerodynamics work, particularly through Fusion 360 knowledge.

RACI CHART

The RACI matrix allows the team to visualise participation in all tasks. RevolutionX modified the standard Responsible, Accountable, Consulted and Informed categories into three categories: Responsible, Informed and Excluded.

CODE	MEANING	USE IN REVOLUTIONX
R	Responsible	Member directly working on or leading the task.
I	Informed	Member kept updated because the task affects their area.
E	Excluded	Member not involved in the task.

DEPARTMENT	TYPICAL RESPONSIBLE ROLES	TYPICAL INFORMED ROLES
Sponsorship	Saul, Martina, Claudia	Team coordinators, sponsors
Engineering	Martin, Victor, Alvaro, Ibrahim	Business team, mentor
Publicity	Yago, Martina, Claudia	Sponsors, followers
Documents	Saul, Martin, Martina, Yago	Team members and coordinators

TEAM & STAKEHOLDERS

STAKEHOLDER REGISTER

A stakeholder is any person, group or organisation that has an interest in or is affected by a project. Identifying stakeholders was the first step in RevolutionX's communication strategy because it allowed the team to communicate more effectively and deliberately.

After research and analysis, RevolutionX identified nine stakeholders: the team coordinators, team members, mentor, press, competition judges, followers, Nova Alliance members, sponsors and Owla, the team that co-founded Nova Alliance with RevolutionX.

STAKEHOLDER	WHY THEY MATTER
Coordinators	They control project direction, tasks and budgets.
Team members	They execute deliverables and need daily operational detail.
Mentor	They advise scope, engineering and project decisions.
Press	They amplify visibility and brand awareness.
Judges	They assess the final project at competition.
Followers	They provide community visibility and engagement.
Nova Alliance	They support international collaboration.
Owla	They co-founded Nova Alliance with RevolutionX.
Sponsors	They provide resources and require clear ROI communication.

COMMUNICATION TOOLS

Matching tools to stakeholders ensures that each stakeholder feels comfortable communicating with the team. RevolutionX uses different tools depending on urgency, relationship and content type.

TOOL	STAKEHOLDERS	FREQUENCY
WhatsApp	Team members, coordinators and sponsors	Daily
Telegram	Team members, coordinators, mentor and Owla	Weekly
Instagram	Followers, sponsors and members of Nova Alliance	Monthly
Gmail	Team members, coordinators, mentor and sponsors	Weekly
ClickUp	Team coordinators	Weekly

INTERNAL COMMUNICATION PLAN

AUDIENCE	INFORMATION COMMUNICATED	FREQUENCY
Team members	Project details, timelines, scope and budget	Daily
Coordinators	Project details, timelines, scope and budget	Weekly
Mentor	Project details, scope and budget	Weekly

EXTERNAL COMMUNICATION PLAN

AUDIENCE	INFORMATION COMMUNICATED	FREQUENCY
Sponsors	Project details and budget	Quarterly
Owla	Nova Alliance details and management	Monthly
Nova Alliance members	Nova Alliance details	Monthly
Followers	Instagram posts	Monthly

The plan defines the relationship maintained with each stakeholder group. Internal communication focuses on coordination and execution, while external communication focuses on visibility, partnership, sponsorship and alliance management.

COMMUNICATION MAP		
Daily execution	Weekly control	Monthly visibility
Quarterly sponsors	Alliance contact	Press outreach

RISK IDENTIFICATION, PLANNING, ANALYSIS & ASSESSMENT

One of the biggest challenges RevolutionX faced was identifying risks and errors and deciding how to manage them properly. To address this, the team anticipated mistakes in advance and built in time and budget margins so possible setbacks could be solved quickly.

The team also used the main issues encountered during the regional competition as a reference point to prevent them from happening again at the national finals. These risks affected every area of the project, from car manufacturing to the pit display.

MONITORING & CONTROLLING

A status report is a monthly review of completed and pending tasks, allowing the team to maintain consistent organisation. The Enterprise Coordinator prepares a monthly status report for RevolutionX.

CONTROL ARTIFACT	PURPOSE	OWNER
Status report	Review completed and pending tasks each month	Enterprise Coordinator
Budget tracking	Compare available and required funds	Business management
Schedule updates	Keep the Gantt chart aligned with deadlines	Coordinators
Risk list	Track engineering, marketing and pit display threats	All sectors

ENGINEERING RISKS

RISK	IDENTIFIED ISSUE	SOLUTION
Car protection	Potential car breakage before the competition	Purchase a padded case
Sticker dimensions	Missing or incorrect sticker dimensions on the car	Verify dimensions in Fusion 360 and use multiple sketches with different sizes
Car production	Potential car breakage during CNC milling	Have a 3D-printed backup design ready
Simulations	Simulations not ready in time for the Engineering Portfolio	Prioritise simulations over secondary tasks
Car weight	Excessively high car weight, as happened at the nationals	Purchase lower-density bearings

ENGINEERING RESPONSE LOGIC

- >> Critical risks are handled before competition because they can block participation entirely.
- >> Fusion 360 is used as a preventive check for stickers, dimensions and engineering verification.
- >> Backup manufacturing reduces dependency on a single CNC outcome.
- >> Simulation work is prioritised because it directly affects the Engineering Portfolio.

MARKETING RISKS

RISK	IDENTIFIED ISSUE	SOLUTION
Sponsors	Not having enough sponsors for the competition	Turn to closer, more accessible sponsors to ensure a strong brand identity
Brand awareness	Not promoting the brand enough to be recognised	Highlight the logo on the pit display, get featured in newspapers and attend STEM Racing events such as Cupra City Garage
Budget	Not having enough funding for the project	Maintain organisational budget tracking with available and required funds

PIT DISPLAY RISKS

RISK	IDENTIFIED ISSUE	SOLUTION
Element deadlines	Not having all pit display elements ready on time	Order elements as early as possible and build a time buffer for printing errors
Poster resolution	Printed posters having low resolution	Consult the printing company for feedback and adjust files if any issues appear

RISK AREAS 3	MAIN CONTROLS Time + budget
REPORT CYCLE Monthly	SOURCE LESSON Regionals

NAME

Choosing a team name was one of the first steps in developing RevolutionX's brand identity. The team wanted the name to be in English to maintain international appeal. This ensures that if the team qualifies for the World Finals, no rebrand will be needed.

The final choice was "RevolutionX". The word "Revolution" has a double meaning: it can represent modernity and change, and it can also refer to the revolutions, or RPM, made by a car's wheels. The capital X at the end gives the name a unique, modern and alternative edge.

COLOUR SCHEME

Colours are central to a company because they help the public remember it. RevolutionX chose black and gold. These colours represent elegance and professionalism, and they are highly distinguishable. For graphic elements such as the logo, the team uses a gold gradient that mixes darker and lighter gold to create a bright effect.

BLACK

GOLD

GOLD GRADIENT

LOGO

The RevolutionX logo was one of the graphic elements prioritised most during brand development. After numerous sketches, the team arrived at its official design: a tyre-shaped circle with the team name placed directly in the centre. The logo can be displayed with a solid black background or a transparent background.

LOGO WITH
BACKGROUND

LOGO
WITHOUT
BACKGROUND

Logo use is tied to the brand system: black, gold, circular tyre reference and a clear RevolutionX wordmark.

UNIFORM

When deciding on uniform design, RevolutionX wanted something simple yet representative of the brand. The first decision was the type of shirt. The team chose a polo shirt because it balances professionalism and comfort.

The design remains deliberately simple: black with gold stripes on the shoulders. The shirts were produced by one of the team's sponsors, who provided the manufacturing service free of charge.

UNIFORM SYSTEM

RX

FRONT: BLACK POLO + GOLD SHOULDERS

REVOLUTIONX
MEMBER ROLE

BACK: SPONSOR VISIBILITY

MARKETING GOALS

Before executing marketing projects, RevolutionX first established the objectives behind each task. This kept the work focused on the goals and prevented the team from straying off track.

- >> Increase project visibility.
- >> Raise awareness about STEM Racing.
- >> Collaborate with other teams in the competition.
- >> Partner with sponsors.


TARGET AUDIENCES

TARGET	CHARACTERISTICS	MARKETING TASKS	EXPECTED RESULTS
Students	Age 11-19, male and female, social media users, colloquial language	Instagram posts	Increase participation in STEM Racing
General public	All ages, male and female, worldwide, formal language	Newspaper articles	Increase visibility
Potential sponsors	Age 25+, male and female, formal language	Direct communication by email or Instagram DMs	Increase resources
STEM Racing teams	Age 11-19, male and female, colloquial language	Direct communication and collaborations	A community of teams for questions and visibility

TAKING ACTION - INSTAGRAM

Instagram is the social media platform RevolutionX uses to share posts promoting the team and sponsors. It is also a communication channel for contacting companies and sending the sponsorship proposal. Through Instagram, the team also established Nova Alliance.

METRIC	PRIORITY ORDER
Goals	1, 2, 4 and 3
Target audience	2, 3, 1 and 4



WEBSITE

The Engineering Coordinator designed a website used to share information about the team and sponsors. The website targets the general public, students, potential sponsors and other STEM Racing teams.


WEBSITE FIELD	DEFINITION
Goals	1, 2 and 4
Target audience	2, 1, 3 and 4
Content purpose	Explain the team, sponsors, STEM Racing and brand identity

NOVA ALLIANCE

Together with the Spanish team Owla, RevolutionX created Nova Alliance, an international alliance of STEM Racing teams from around the world. The goal is to support one another, resolve questions and increase collective visibility.

TEAM	COUNTRY	ROLE
RevolutionX	Spain	Co-founder
Owla	Spain	Co-founder
Buffalo Six	Mexico	Member
Team Stealth	Wales	Member
Vielox	Vietnam	Member
Apex Elegance	China	Member

NOVA ALLIANCE FIELD	PRIORITY ORDER
Goals	3, 2 and 1
Target audience	4, 2 and 1



HIGH SCHOOL OPEN HOUSE

During the school's Open House, where many children came to explore the facilities and educational programmes, RevolutionX introduced its STEM Racing team to them.

FIELD	VALUE
Goals	1 and 2
Target audience	1 and 2
Purpose	Introduce STEM Racing to students and the general school community

NEWSPAPER ARTICLES

The Head of Strategy, Engineering and External Relations connected with a journalist from EL MUNDO after contacting several newspapers. After gathering information about RevolutionX, the journalist published an article in the GranMadrid section.

Following this press coverage, other media outlets showed interest. The team hosted a presentation where they could ask questions. A major highlight was the attendance of local mayor Lola Moreno.

FIELD	VALUE
Goals	1 and 2
Target audience	2, 1, 4 and 3

MEDIA OUTLETS

RevolutionX has been featured in multiple media outlets, expanding visibility and strengthening the team's public identity.

EL MUNDO	RNE
El Espanol	InfoMajadahonda
Noroeste Madrid	Majadahonda Magazine
Additional media outlets	

VISIT BY THE MAYOR OF MAJADAHONDA

On February 24th, Lola Moreno, the mayor of Majadahonda, visited the high school with several media outlets and Cristina Benzal, Director of Formula MadCup - STEM Racing Spain. During the visit, RevolutionX delivered a presentation about the team and STEM Racing.

After this meeting, the city council offered to sponsor RevolutionX.

FIELD	VALUE
Goals	4, 1 and 2
Target audience	3 and 2
Result	City council sponsorship offer

PUBLICITY LOGIC

The media and event strategy connects several objectives: increasing visibility, explaining STEM Racing, reaching potential sponsors and strengthening public trust in the team. Press coverage, school events and institutional visits all feed into a stronger brand identity.

PUBLIC IMPACT CHAIN	
OUTREACH	Contact newspapers, school audiences and institutions.
COVERAGE	Articles and presentations make the team visible beyond the competition.
CREDIBILITY	Public attention validates the seriousness of the project.
RESOURCES	Visibility supports sponsorship and future partnerships.

SPONSORS AND INSTITUTIONAL SUPPORT



RESOURCES

SPONSORSHIP OVERVIEW

RevolutionX currently has four monetary sponsorship contributors totalling 625 EUR and three material sponsorship contributors providing 10 uniforms and 3 roll-ups.

Sponsor Type	Contribution	Sponsors
Monetary	625 EUR	Panalon, Lorena Solutions, Monita, Titanes and El Postrecito de Isabel
Material	10 uniforms + 3 roll-ups	Black & White, Majadahonda City Council and El Postrecito de Isabel

The team estimated that it needed 1000 EUR to cover project expenses. The most obvious initial idea was to secure the money through sponsors, so RevolutionX began its sponsorship search.

SPONSORS AND INSTITUTIONAL SUPPORT



SPONSORSHIP STRATEGY

The sponsorship strategy was built around obtaining the resources required for the national finals while protecting a strong brand identity. The team focused on accessible sponsors and built relationships with companies that showed genuine interest.

Step	Recruitment Phase	Execution
1	Initial outreach	Send the sponsorship proposal to as many companies as possible. Most companies did not reply or were not interested, so only interested companies moved forward.
2	Nurturing relationships	Build relationships with potential sponsors by discussing the project, required resources and collaboration possibilities.
3	Sponsorship confirmation	Officially and publicly announce each confirmed partnership agreement.

RETURN ON INVESTMENT (ROI)

ROI measures the benefit gained relative to the amount invested. Because RevolutionX found alternative ways to secure resources, especially crowdfunding, the team did not take on a massive number of sponsors. This allowed every sponsor logo to appear on almost every representative element: shirts, car, roll-ups and pit display.

The size of logos on these items is directly proportional to each company's contribution. This is especially noticeable with the Panalon logo because they contributed 250 EUR, the largest single sponsorship contribution.


GOFUNDME

CROWDFUNDING

Because sponsorship money alone was not enough to cover the expected budget and the search for more sponsors was long and costly, RevolutionX looked for alternative fundraising methods. After brainstorming, the team decided to launch a crowdfunding campaign.

The next day, RevolutionX launched its own GoFundMe campaign asking for 1000 EUR. The results were almost immediate. Although the team did not reach the full 1000 EUR target, it raised enough money to cover expenses: 625 EUR.

Crowdfunding Target	Money Raised
1000 EUR	625 EUR
Largest Sponsor	Final Spend
250 EUR	1033 EUR

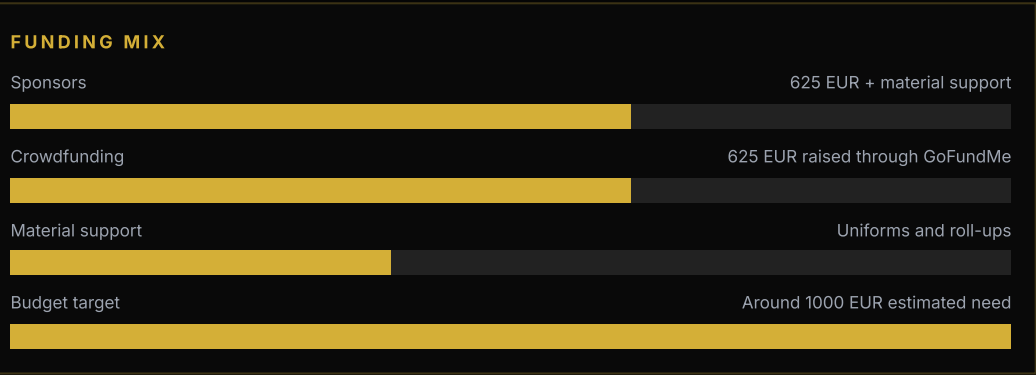

SUSTAINABILITY OVERVIEW

RevolutionX considered it imperative to undertake projects that contribute, in some capacity, to preserving the planet. The team identified environmental challenges in its immediate surroundings and concluded that the two most pressing issues were water-borne microplastics and environmental heavy metal toxicity.

To address these concerns, RevolutionX initiated the standardisation of biodegradable PLA and organised a battery collection campaign.

ENVIRONMENTAL ISSUES

MICROPLASTICS

Plastic consumption leads to microplastics reaching landfills and oceans. The team responded by increasing PLA use.

HEAVY METALS

Improper battery disposal can contaminate soil and water with hazardous metals. The team responded with a collection campaign.

BIODEGRADABLE PLA


One of the most significant environmental issues facing the planet is the presence of microplastics in water. Plastic is widely used across many industries, and this consumption sends microplastics to landfills and eventually oceans.

According to data published by Pennsylvania State University in its 2024 Science of the Total Environment study on microplastic accumulation, recycled plastic has increased since 1950, yet only 8% of plastics are actually recycled, with most ending up in landfills.

PLA IMPLEMENTATION

Because of the environmental problems caused by plastics, RevolutionX made a conscious effort to minimise non-biodegradable materials. The team increased its use of PLA, which is biodegradable and compostable, leaving no lasting footprint.

Several members personally invested in 3D printers. Although intended for personal use, these printers were made available to the team to produce test cars and keychains for competition day. Moving away from regular plastic use ensured the team's operations did not contribute to ocean microplastic pollution.

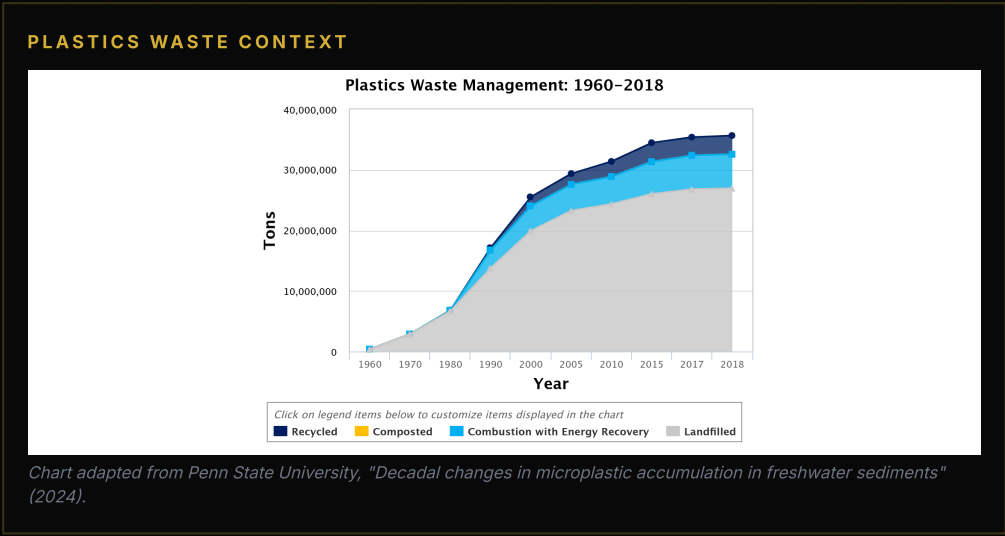

BATTERY COLLECTION CAMPAIGN

The electronics sector is one of the largest sources of environmental pollution. A systematic review in the International Journal of Environmental Research and Public Health explains that electronic waste, including batteries, contains hazardous materials that severely contaminate the environment when not managed correctly.

The main issue is that these components often end up in illegal landfills or are improperly processed, leading to heavy metals such as lead, mercury, cadmium, arsenic and chromium leaching into soil and water.

In response, RevolutionX launched a battery collection campaign at the high school. The team collected approximately 1,000 batteries and delivered them to the local municipal waste management centre to be processed according to safety regulations, preventing ecosystem damage.

BATTERIES COLLECTED

1000

MATERIAL FOCUS

PLA

PLASTIC RECYCLE RATE CITED

8%

HAZARD CONTROLLED

Heavy metals

ENTERPRISE PORTFOLIO COMPLETION

This enterprise portfolio preserves the complete original content structure: project management, scope, WBS, schedule, budget, roles, RACI, communications, risks, monitoring, identity, marketing, sponsorship, crowdfunding and sustainability. The information is presented in a denser A3 format aligned with elite reference portfolios while keeping RevolutionX's black and gold brand identity.
